

Transfer FATP line plan from F16 1stF to F07 3rdF




QUANG CHAU ZONE M&F




Transfer line routing



Current line at F16 1stF

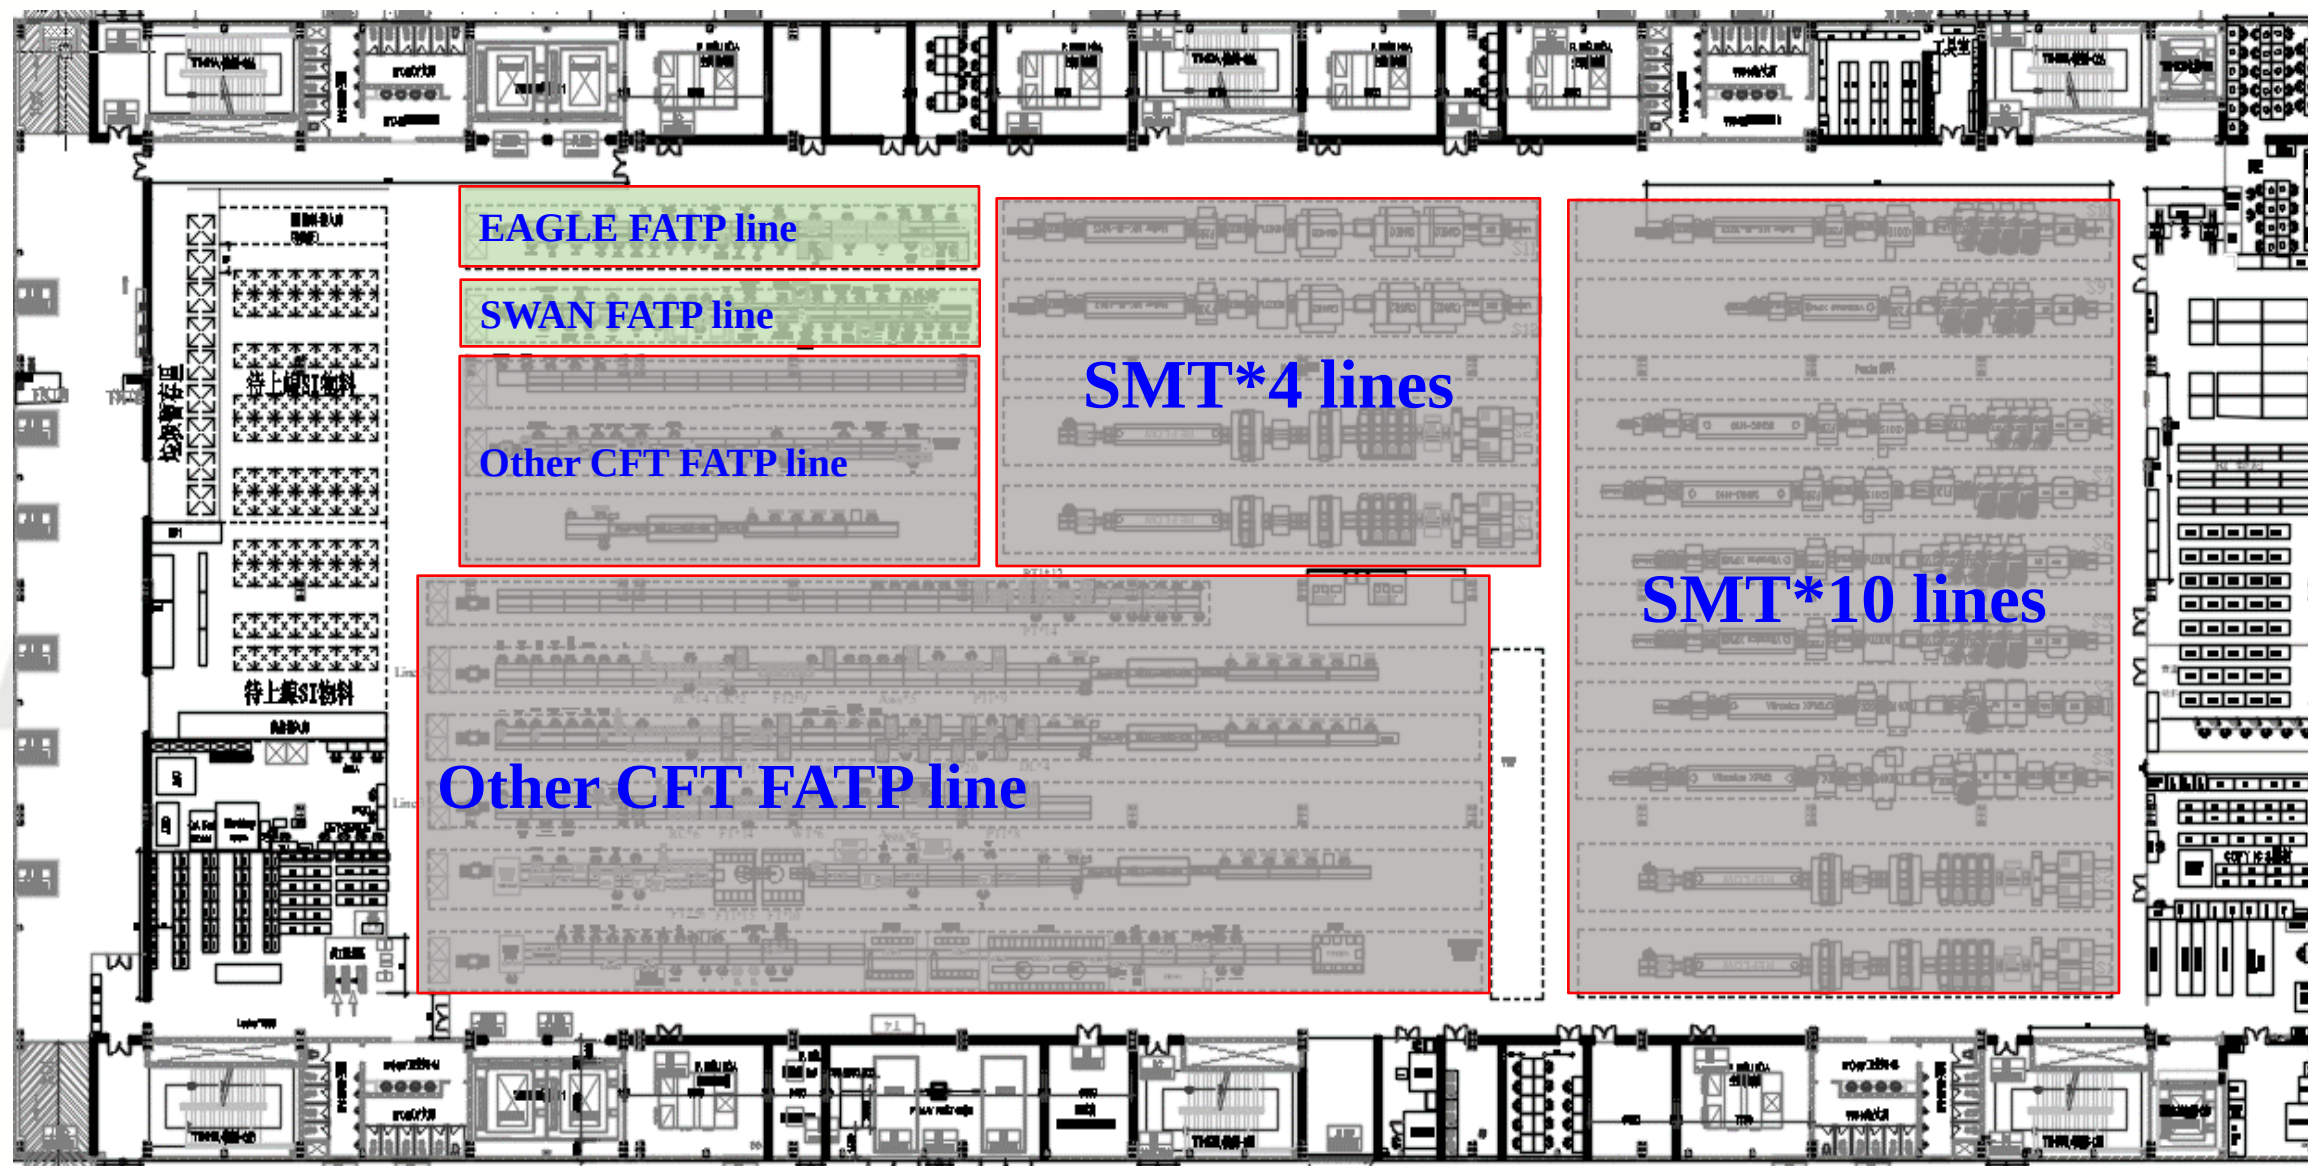


FATP Line at F07 3rdF

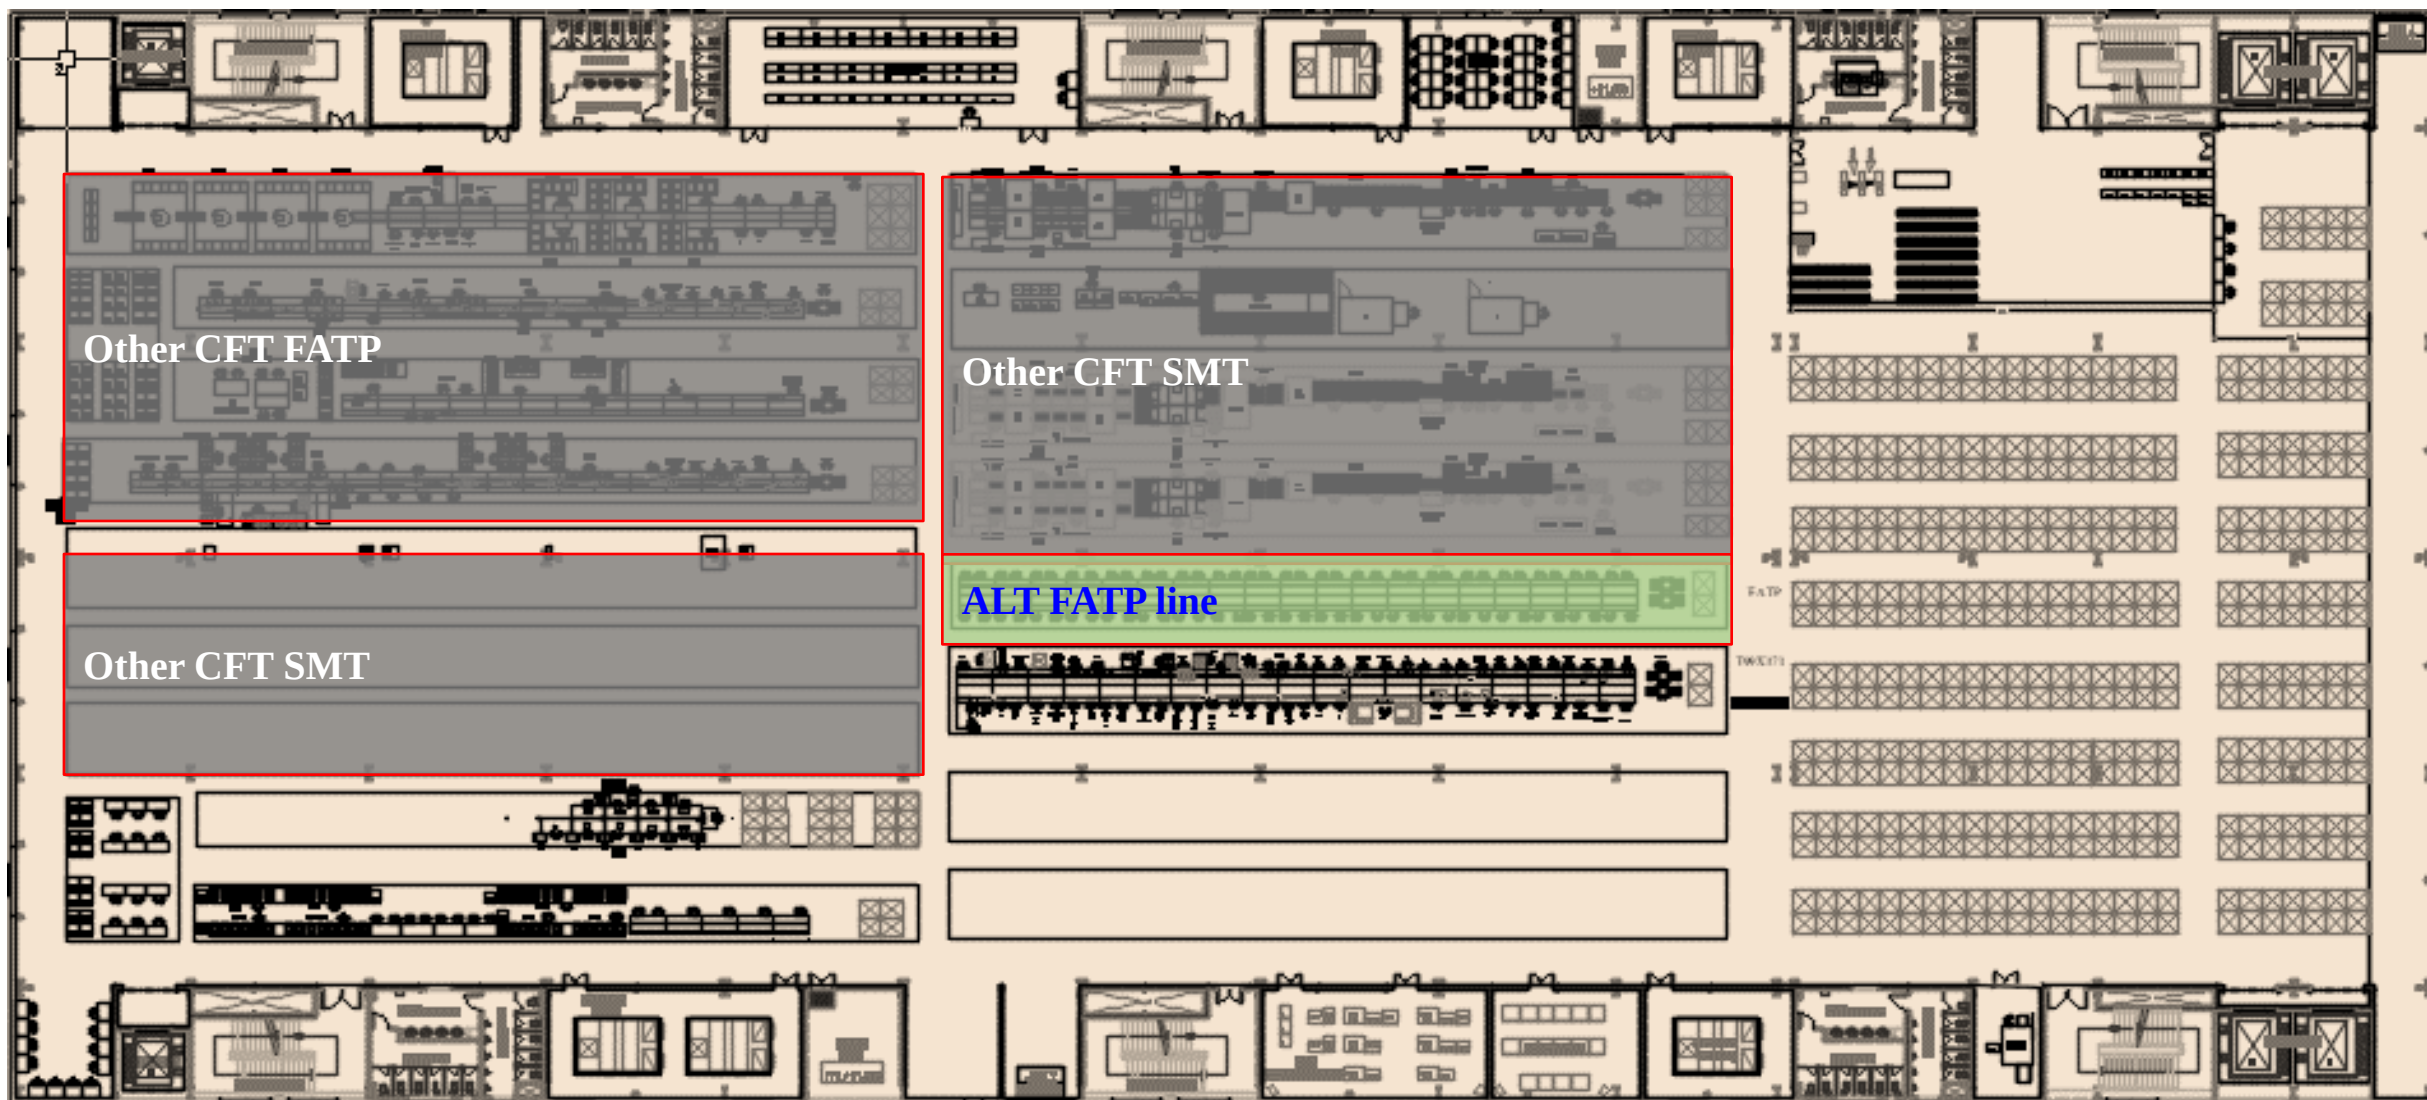


SMT&DIP line keep in F16

Detail FATP Line at F07 3rdF

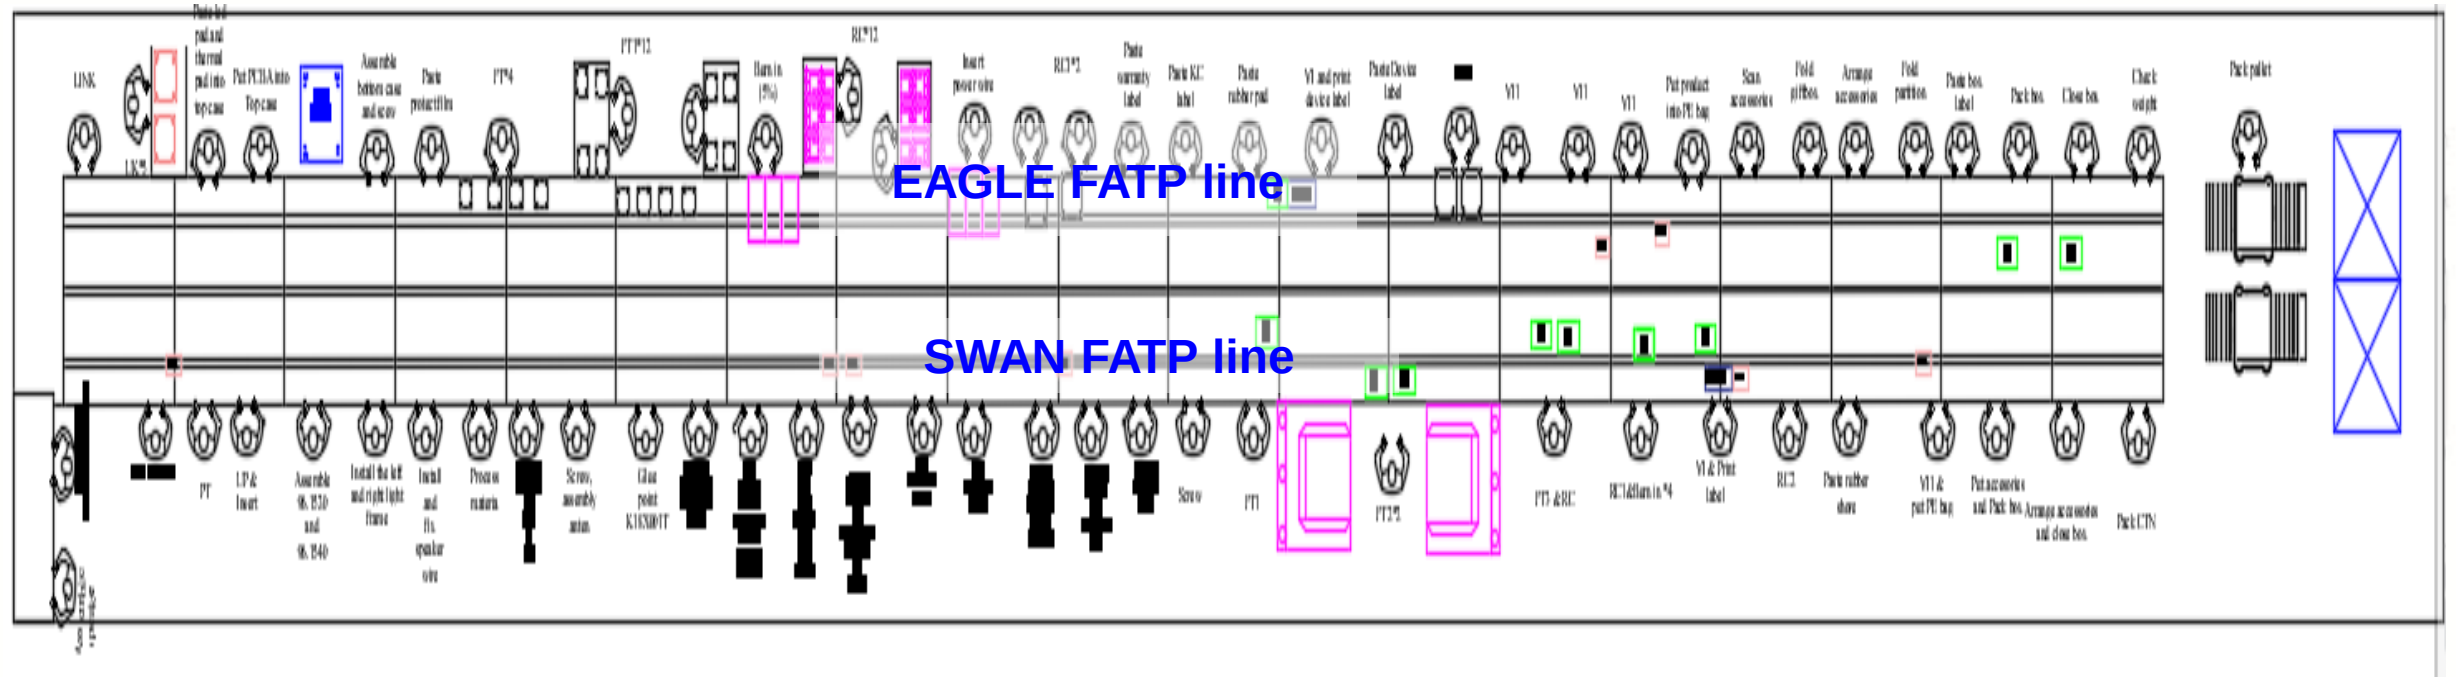

Transfer FATP from F16-1F to F07-3F milestone

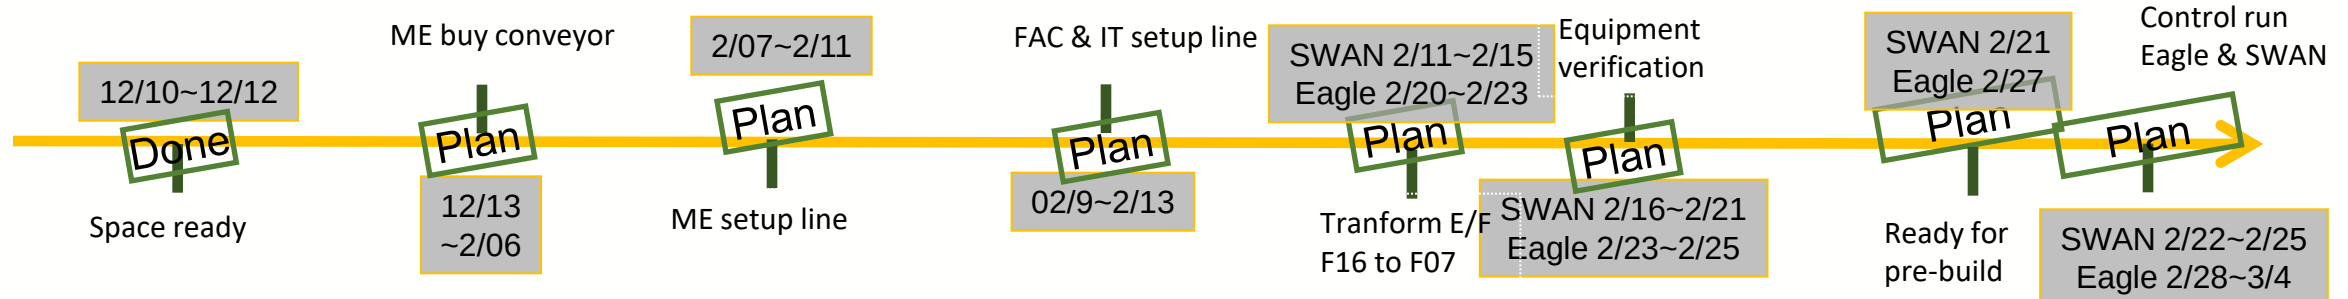

No	Line	Item	Thu 2/2	Fri 2/3	Sat 2/4	Sun 2/5	Mon 2/6	Tue 2/7	Wed 2/8	Thu 2/9	Fri 2/10	Sat 2/11	Sun 2/12	Mon 2/13	Tue 2/14	Wed 2/15	Thu 2/16	Fri 2/17	Sat 2/18	Sun 2/19	Mon 2/20	Tue 2/21	Wed 2/22	Thu 2/23	Fri 2/24	Sat 2/25	Sun 2/26	Mon 2/27	Tue 2/28	Wed 3/1	Thu 3/2	Fri 3/3	Sat 3/4	Sun 3/5
1	ALT FATP Line	Space ready																																
2		ME buy conveyor line																																
3		Set up line																																
4		Fac Setup and IT Setup																																
5		Transfer SWAN E/F from F16 to F07																																
6		Equipment verification																																
7		Ready for pre-build																																
8		Control run SWAN 100pcs																																
9		Gage Repeatability & Reproducibility																																
10		SWAN Ready for MP																																
11		MP Eagle for 28K in F16(Original line)																																
12		Transfer Eagle E/F from F16 to F07																																
13		Set up Equipment and verification																																
14		Ready for pre-build																																
15		Control run Eagle 100pcs																																
16		Gage Repeatability & Reproducibility Report																																
17		Eagle Ready for MP																																

Done

Holiay

Plan

Function	Name	Email	Note
MFG PM	Yuri	yuri.yr.ruan@mail.foxconn.com	No change
MPM	Kiara	kiara.sl.nguyen@mail.foxconn.com	
PQE	Robert	robert.wb.wu@mail.foxconn.com	
QE	ken.sv.pham	ken.sv.pham@mail.foxconn.com	
PE	Michael	cpe-vn-pe-npi@mail.foxconn.com	
ME	Cheng Lun	cheng-lun.ruan@mail.foxconn.com,	
TE	Allan	allan.wq.pham@mail.foxconn.com	
PD	Nga	cpe-vn-rma@mail.foxconn.com,	
IE Engineer	Trang	cpe-vn-ie-01@mail.foxconn.com	
IQC	Ms. Quyen	cmb-vn-iqc@mail.foxconn.com	
SQE	Ha	cpe-vn-sqe@mail.foxconn.com	
PC-FATP	Nhai	cpe-vn-pc-02@mail.foxconn.com	
PC-SMT	Quyết	cpe-vn-pc-smt@mail.foxconn.com	

1. IDL as list above
2. DL as file attach:



SWAN DL list



Eagle DL list

Equipment & Fixture list transfer

Equipment Name	Usage	Qty
Test Computer	Common	35
IQM8W/IQXeI 80	Common	1.25
4K TV	Unique	7
Soundbar shieldling box	Common	2
BT Test fixture	Unique	5
FT1 Test fixture	Unique	4
RC Test fixture	Unique	2
RC1 Test fixture	Unique	2
RC2 Test fixture	Unique	2
Barcode reader	Common	17
4K HDMI 30hz MAGIC card	Unique	4
HDMI 60hz MAGIC card	Unique	13
Network card	Common	50
Camera 2.0	Common	24
USB 3.0	Common	19
Audio 3.5	Common	17
usb 3.0 cable	Common	21
control board	Common	20
Cable Jum 4pin	Common	44
Micro usb	Common	68
Speaker	Common	9
power connector	Consumable	54
connector 5521 1/2公对母	Consumable	54
RF connector	HIROSE	5
RF cable	woken	10
PCI Com card	Common	22
ETH cable	Consumable	54
Adapter-48 VDC	Local	68
HDMI cable	Consumable	21
BT golden	Consumable	10
Remote box	Consumable	20

SWAN E&F transfer list

Equipment Name	Usage	Qty
Test Computer	Common	40
Test Computer	Common	4
4K TV		1
Shielding box	Common	14
UK Test fixture	Unique	5
FT Test fixture	Unique	4
FT1 Test fixture	Unique	13
RC Test fixture	Unique	12
RC1 Test fixture	Unique	2
RC2 Test fixture	Common	2
Barcode reader	Unique	35
HDMI 60hz MAGIC card	Unique	4
Aver Media card 30hz	Common	4
Network card	Common	80
Camera 2.0	Common	40
USB 3.0	Common	23
Audio 3.5	Common	19
usb 3.0 cable	Common	25
control board		40
Cable Jum 4pin		70
5521 1/2 1公对2母	Common	93
Com card	Common	40
AP access point	Common	19
change COM USB cable	Consumable	18
ETH cable	Consumable	82
AC/DC converter 230V AC-12V DC	Consumable	124
HDMI cable	Consumable	35
BT golden	Consumable	20
Remote box	Consumable	29

Eagle E&F transfer list
